

	(A)	Nombre	Duracion	Inicio	Terminado	Predecesores
1		PROYECTO	54 days?	11/09/18 10:00 AM	26/11/18 10:00 AM	
2		Analisis y Requisitos	1 day?	11/09/18 10:00 AM	12/09/18 10:00 AM	
3	Ö	Entrevista con el usuario	1 day?	11/09/18 10:00 AM	12/09/18 10:00 AM	
1		Diseño y Arquitectura	5 days?	12/09/18 10:00 AM	19/09/18 10:00 AM	
5		Planeacion del desarrollo del proyecto	2 days?	12/09/18 10:00 AM	14/09/18 10:00 AM	3
6	Ö	Planeacion del diseño de la pagina	2 days?	14/09/18 10:00 AM	18/09/18 10:00 AM	5
7		Distribucion de Trabajo	1 day?	18/09/18 10:00 AM	19/09/18 10:00 AM	6
8		Programacion	24 days?	19/09/18 10:00 AM	23/10/18 10:00 AM	
9		Programacion HTML & CSS	13 days?	19/09/18 10:00 AM	8/10/18 10:00 AM	7
10		Programacion JavaScript	11 days?	8/10/18 10:00 AM	23/10/18 10:00 AM	9
11		Pruebas	8 days?	23/10/18 10:00 AM	2/11/18 10:00 AM	
12		Comprobacion de bugs y errores	3 days?	23/10/18 10:00 AM	26/10/18 10:00 AM	10
13		Reunion una vez mas con el usuario	1 day?	26/10/18 10:00 AM	29/10/18 10:00 AM	12
14		Correccion o adicion de nuevas cosas	4 days	29/10/18 10:00 AM	2/11/18 10:00 AM	13
15		Programacion	4 days	2/11/18 10:00 AM	8/11/18 10:00 AM	
16		Diseño del diagrama ER	1 day	2/11/18 10:00 AM	5/11/18 10:00 AM	14
17		Hacer Querys (tablas con sus respecti	3 days	5/11/18 10:00 AM	8/11/18 10:00 AM	16
18		Pruebas	1 day?	8/11/18 10:00 AM	9/11/18 10:00 AM	
19		Comprobacion de bugs y errores	1 day?	8/11/18 10:00 AM	9/11/18 10:00 AM	17
20		Programacion	9 days?	9/11/18 10:00 AM	22/11/18 10:00 AM	
21		Implementar la BD a la pagina web	3 days?	9/11/18 10:00 AM	14/11/18 10:00 AM	19
22		Retoques Finales	5 days?	14/11/18 10:00 AM	21/11/18 10:00 AM	21
23		Subir la pagina al servidor	1 day?	21/11/18 10:00 AM	22/11/18 10:00 AM	22
24		Documentacion	1 day?	22/11/18 10:00 AM	23/11/18 10:00 AM	
25		Documentacion del Proyecto	1 day?	22/11/18 10:00 AM	23/11/18 10:00 AM	23
26		Entrega final del producto	1 day?	23/11/18 10:00 AM	26/11/18 10:00 AM	
27		Mostrar el producto al cliente	1 day?	23/11/18 10:00 AM	26/11/18 10:00 AM	25
28		Programacion	5.5 days?	20/09/18 08:00 AM	27/09/18 01:00 PM	
29	Ö	Programacion de HTML con Bootstrap	5.5 days?	20/09/18 08:00 AM	27/09/18 01:00 PM	7
30		Documentacion	5 days?	22/10/18 08:00 AM	26/10/18 05:00 PM	
31	O	Correccion de entrega del primer avance	3.875 days?	23/10/18 09:00 AM	26/10/18 05:00 PM	
	Ö	Diagrama de Comunicacion	5 days	22/10/18 08:00 AM	26/10/18 05:00 PM	
33	Ö	Diagram de Secuencia	2 days?	23/10/18 08:00 AM	24/10/18 05:00 PM	
34	O	Fichas de Casos de Uso	4 days?	23/10/18 08:00 AM	26/10/18 05:00 PM	
	Ö	Archivo de conclusiones		23/10/18 08:00 AM	25/10/18 05:00 PM	

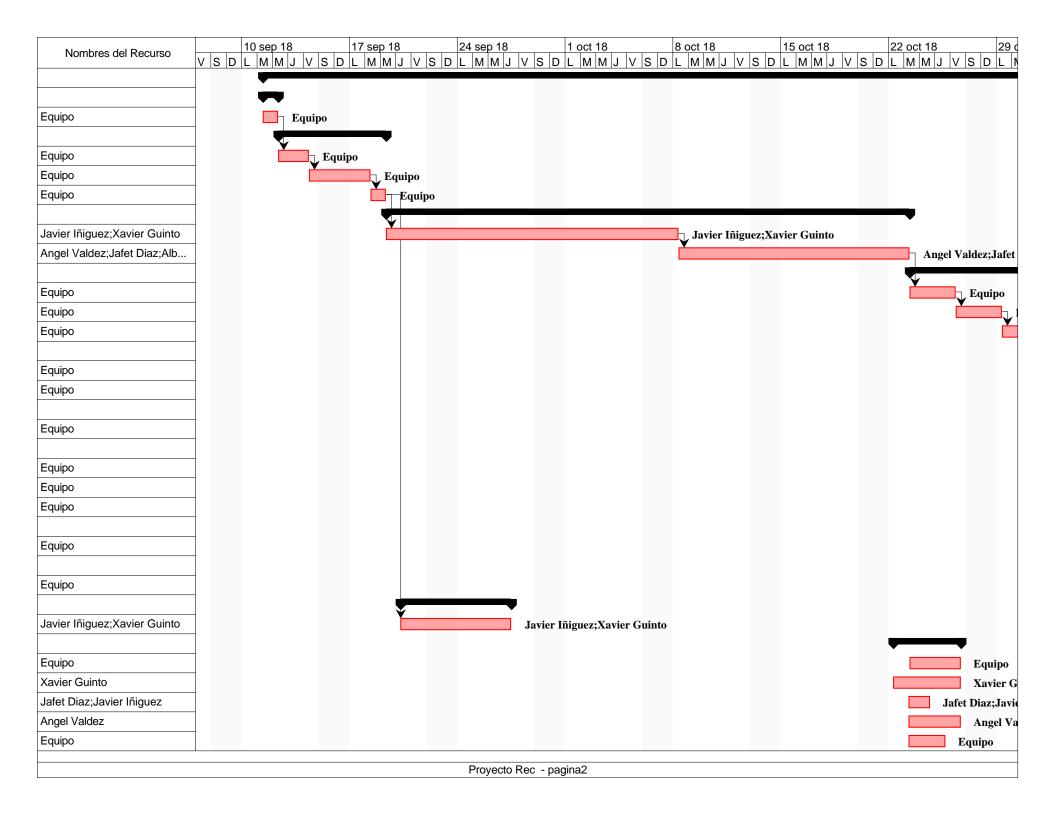

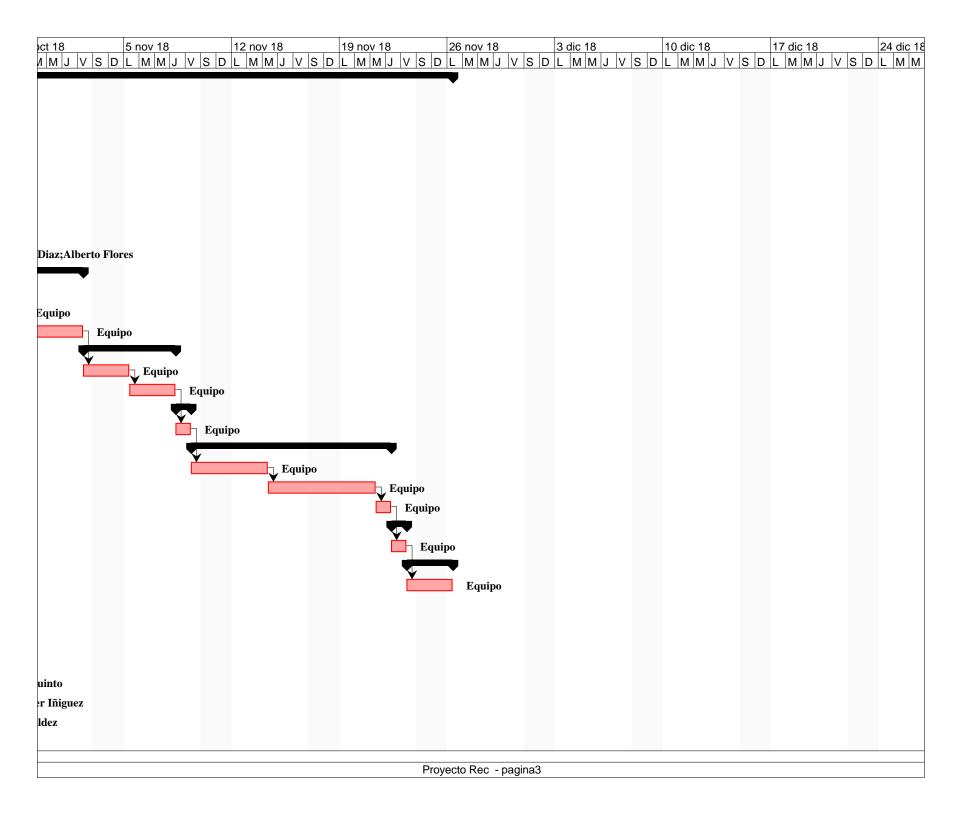

	®	Nombre	Duracion	Inicio	Terminado	Predecesores
						Predecesores
36		Diagrama de estados		24/10/18 08:00 AM	26/10/18 05:00 PM	
37		Diagrama de Componentes	4 days?	23/10/18 08:00 AM	26/10/18 05:00 PM	

Nombres del Recurso	VSD	10 sep 18	V S D I	7 sep 18 M M J V	s D	24 sep 18	V S D	1 oct 18	V S D	8 oct 18	/ S D	15 oct 18	22 o	ot 18	29 d
Alberto Flores	V 0 D		V O D L	- 101 101 0 0	O D	_	V O D		V O D			<u> </u>		101 0 0	Alberto I
Javier Iñiguez															Javier Iñ
<u> </u>													_		001101
						Proyecto F	Rec - pagi	na5							

oct 18	\\ \c \=	5 nov 18 L M M J V S	12 nov 18	3 1	19 nov 18		26 nov 18	3	3 dic 18	10) dic 18	1	7 dic 18		24 dic 18
// M J Tores	V S D	L M M J V S	D L M M .	J V S D L	_ M M J V	SD	L M M J	/ S D L	_ M M J V	S D L	M M J	IV IS ID IL	M M J	V S D	L M M
iguez															
						Drove	ecto Rec - pa	gina6							
						i ioye	colo ivec - ha	giriau							
